



# Grand Panama Towers 1 & 2

Progress Report

7-6-2023

# Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	2022		Qtr 4, 2022			Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023	
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1		<b>Project Duration</b>	<b>230 days</b>	<b>Tue 9/6/22</b>	<b>Mon 7/24/23</b>													
2		<b>Mobilize</b>	6 days	Tue 9/6/22	Tue 9/13/22													
3		<b>Tower 1</b>	<b>114 days</b>	<b>Wed 9/14/22</b>	<b>Mon 2/20/23</b>													
4		North Elevation	25 days	Wed 9/14/22	Tue 10/18/22													
5		East Elevation	7 days	Wed 10/19/22	Thu 10/27/22													
6		West Elevation	7 days	Fri 10/28/22	Mon 11/7/22													
7		South Elevation	75 days	Tue 11/8/22	Mon 2/20/23													
8		<b>Tower 2</b>	<b>170 days</b>	<b>Mon 10/3/22</b>	<b>Fri 5/26/23</b>													
9		North Elevation	7 days	Tue 4/18/23	Wed 4/26/23													
10		West Elevation	22 days	Thu 4/27/23	Fri 5/26/23													
11		South Elevation	20 days	Mon 10/3/22	Fri 10/28/22													
12		East Elevation	40 days	Tue 2/21/23	Mon 4/17/23													
13		<b>Tower 2 Garage</b>	56 days	Mon 5/1/23	Mon 7/17/23													
14		<b>Separate Garage</b>	15 days	Tue 2/21/23	Mon 3/13/23													
15		<b>Tower 2 - Misc. Leak Repairs</b>	20 days	Mon 10/3/22	Fri 10/28/22													
16		Walkways T1 & T2	35 days	Tue 5/30/23	Mon 7/17/23													
17		<b>Demobilize</b>	5 days	Tue 7/18/23	Mon 7/24/23													

- Added the Walkway Coatings CO into the schedule
- Lost Work Days:
  - 9/28/22 – Strong Winds
  - 9/29/22 – Strong Winds
  - 10/13/22 – Rain
  - 10/17/22 – Rain
  - 11/10/22 – Wind/Rain
  - 11/11/22 – Wind
  - 11/15/22 – Wind/Rain
  - 11/25/22 – Fog/Humidity
  - 11/30/22 – Rain
  - 12/8/22 – Heavy Fog/Humidity
  - 12/14/22 – Strong Wind/Rain
  - 12/20/22 – Rain
  - 12/23/22 – Freezing Temperatures
  - 1/3/23 – Rain
  - 1/4/23 – Rain
  - 1/27/23 – Rain
  - 1/30/23 – Heavy Fog/Humidity
  - 1/31/23 – Rain
  - 2/1/23 – Heavy Fog/Humidity
  - 2/2/23 – Rain/Humidity
  - 2/3/23 – Rain/Humidity
  - 3/3/23 – Wind
  - 3/7/23 – Wind
  - 3/13/23 – Rain/Humidity
  - 4/3/23 – Rain
  - 4/13/23 – Rain/Wind
  - 4/14/23 – Rain
  - 4/27/23 – Rain/Wind
  - 6/15/23 – Humidity/Rain
  - 6/19/23 – Rain

Project: Grand Panama - Prelim Date: Thu 7/6/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
Inactive Milestone		Finish-only				




# Areas in Progress

Tower 1 Walkways wall and ceiling paint is complete.

We have begun pressure washing tower 2 walkway ceilings and walls. We will begin painting shortly after.

KEY/LEGEND:	
Complete:	
In Progress:	
Next Location:	

# Swing Stage Drops – Tower 2

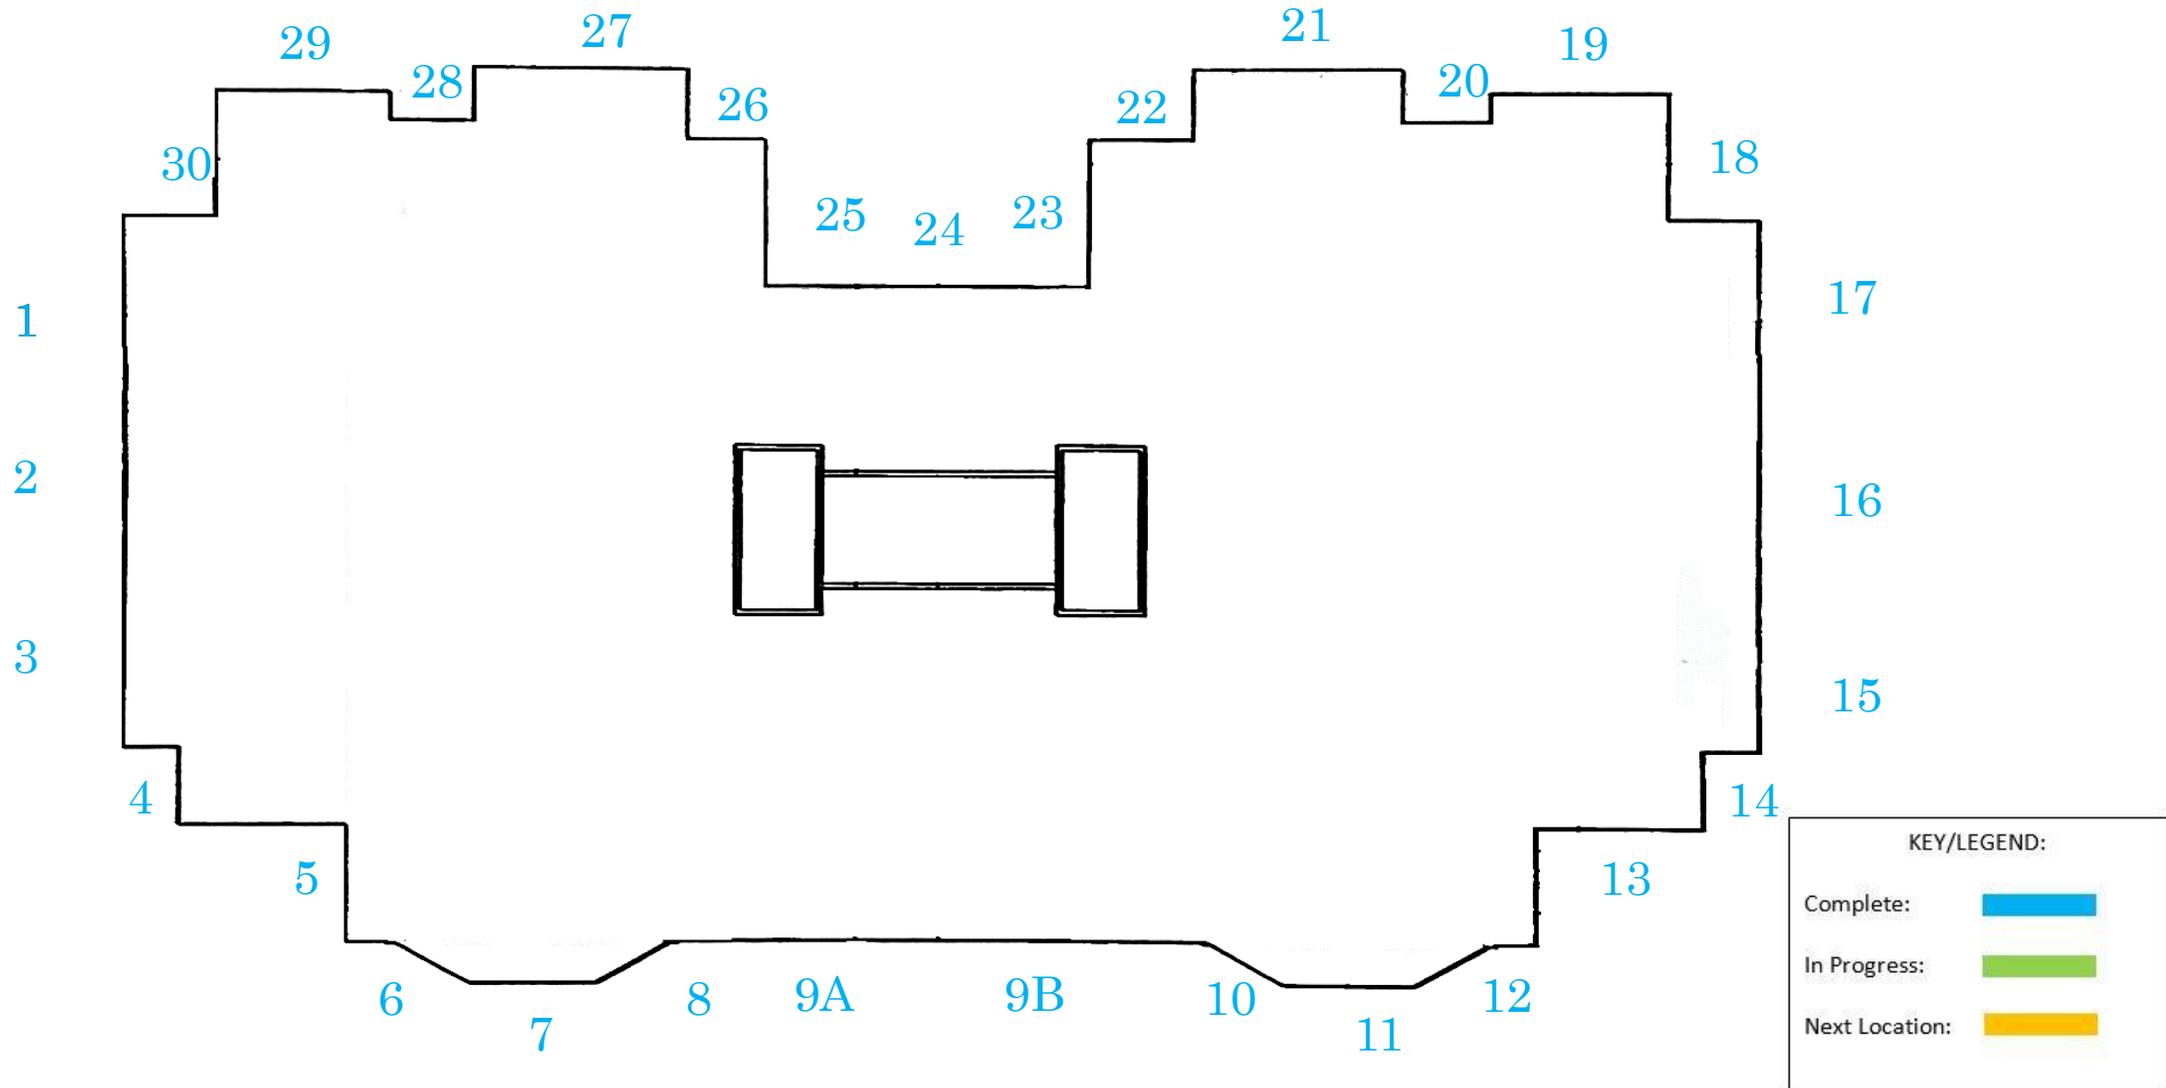

# Swing Stage Drops – Tower 1

