


Grand Panama Beach Resort N Tower Garage Repairs Progress Report

February 13th, 2024

Scope of Work: Surface prep and repairs, coatings

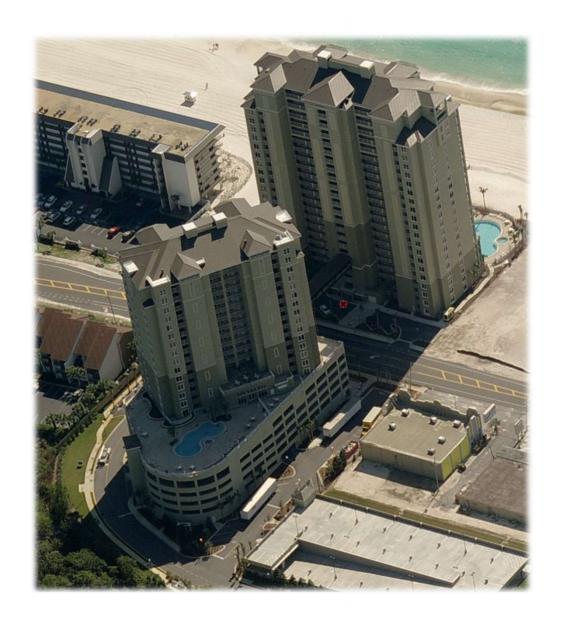



Project Progress



Level 5 deck coating is complete, waiting for traffic striping

Project Progress

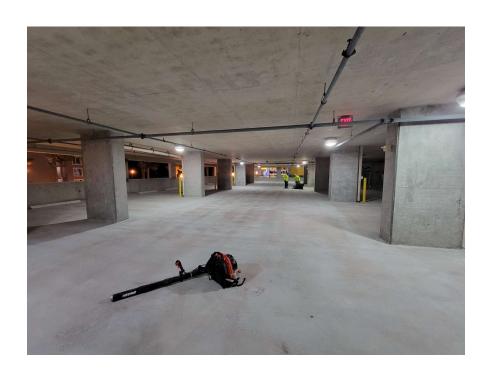

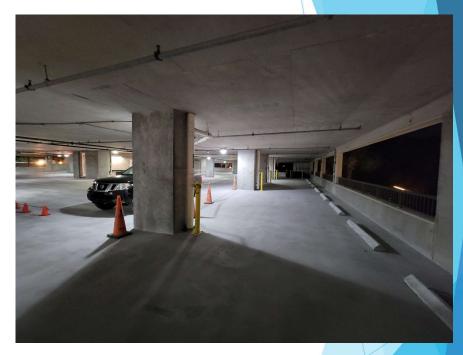

Level 2 - Phase 2 (Outside half), shotblast completed ready for traffic coating.

Grand Panama Beach Resort 2-Week Look Ahead

Week 1: 3/4/24

Level 5 - Traffic striping, open to traffic

Level 2 - Phase 2 deck coating, finish shot blasting deck coating

Level 2 - Phase 3 Complete detail grinding, finish prep for traffic coating, traffic striping

Exit Ramp - finish grinding, surface prep for traffic coating

Week 2: 3/11/24

Level 2 - Phase 2 open to traffic

Level 2 - Phase 3 Traffic coating



Grand Panama Beach Resort Estimated Schedule

Level 5

Grinding Complete 2/15

Deck Coating complete 2/23

Deck Open 3/1

Level 2 - Phase 2

Grinding 2/20
Deck Coating 3/4
Deck Open 3/8

Level 2 - Phase 3

Grinding 2/21

Deck Coating 3/11

Deck Open 3/15





Grand Panama Beach Resort Estimated Schedule

Ramp - Phase 4

Grinding 3/4
Deck Coating 3/15
Deck Open 3/19

Ramp - Phase 5

Grinding 3/4
Deck Coating 3/20
Deck Open 3/24



