



Grand Panama Towers 1 & 2

Progress Report

10-6-22

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	2022											
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
1		Project Duration	189 days	Tue 9/6/22	Fri 5/26/23													
2		Mobilize	6 days	Tue 9/6/22	Tue 9/13/22													
3		Tower 1	89 days	Wed 9/14/22	Mon 1/16/23													
4		North Elevation	30 days	Wed 9/14/22	Tue 10/25/22	2												
5		East Elevation	7 days	Wed 10/26/22	Thu 11/3/22	4												
6		West Elevation	7 days	Fri 11/4/22	Mon 11/14/22	5												
7		South Elevation	45 days	Tue 11/15/22	Mon 1/16/23	6												
8		Tower 2	89 days	Tue 1/17/23	Fri 5/19/23													
9		North Elevation	7 days	Tue 1/17/23	Wed 1/25/23	7												
10		West Elevation	30 days	Thu 1/26/23	Wed 3/8/23	9												
11		South Elevation	7 days	Thu 3/9/23	Fri 3/17/23	10												
12		East Elevation	45 days	Mon 3/20/23	Fri 5/19/23	11												
13		Tower 2 Garage	30 days	Tue 1/17/23	Mon 2/27/23	7												
14		Separate Garage	10 days	Tue 2/28/23	Mon 3/13/23	13												
15		Tower 2 - Misc. Leak Repairs	20 days	Mon 10/3/22	Fri 10/28/22													
16		Demobilize	5 days	Mon 5/22/23	Fri 5/26/23	12												

Project: Grand Panama - Prelim Date: Thu 10/6/22	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Schedule


- No revisions at this time
- Lost Work Days:
 - 9/28/22 – Strong Winds
 - 9/29/22 – Strong Winds



Areas in Progress



Swing Stage Drops – Tower 1

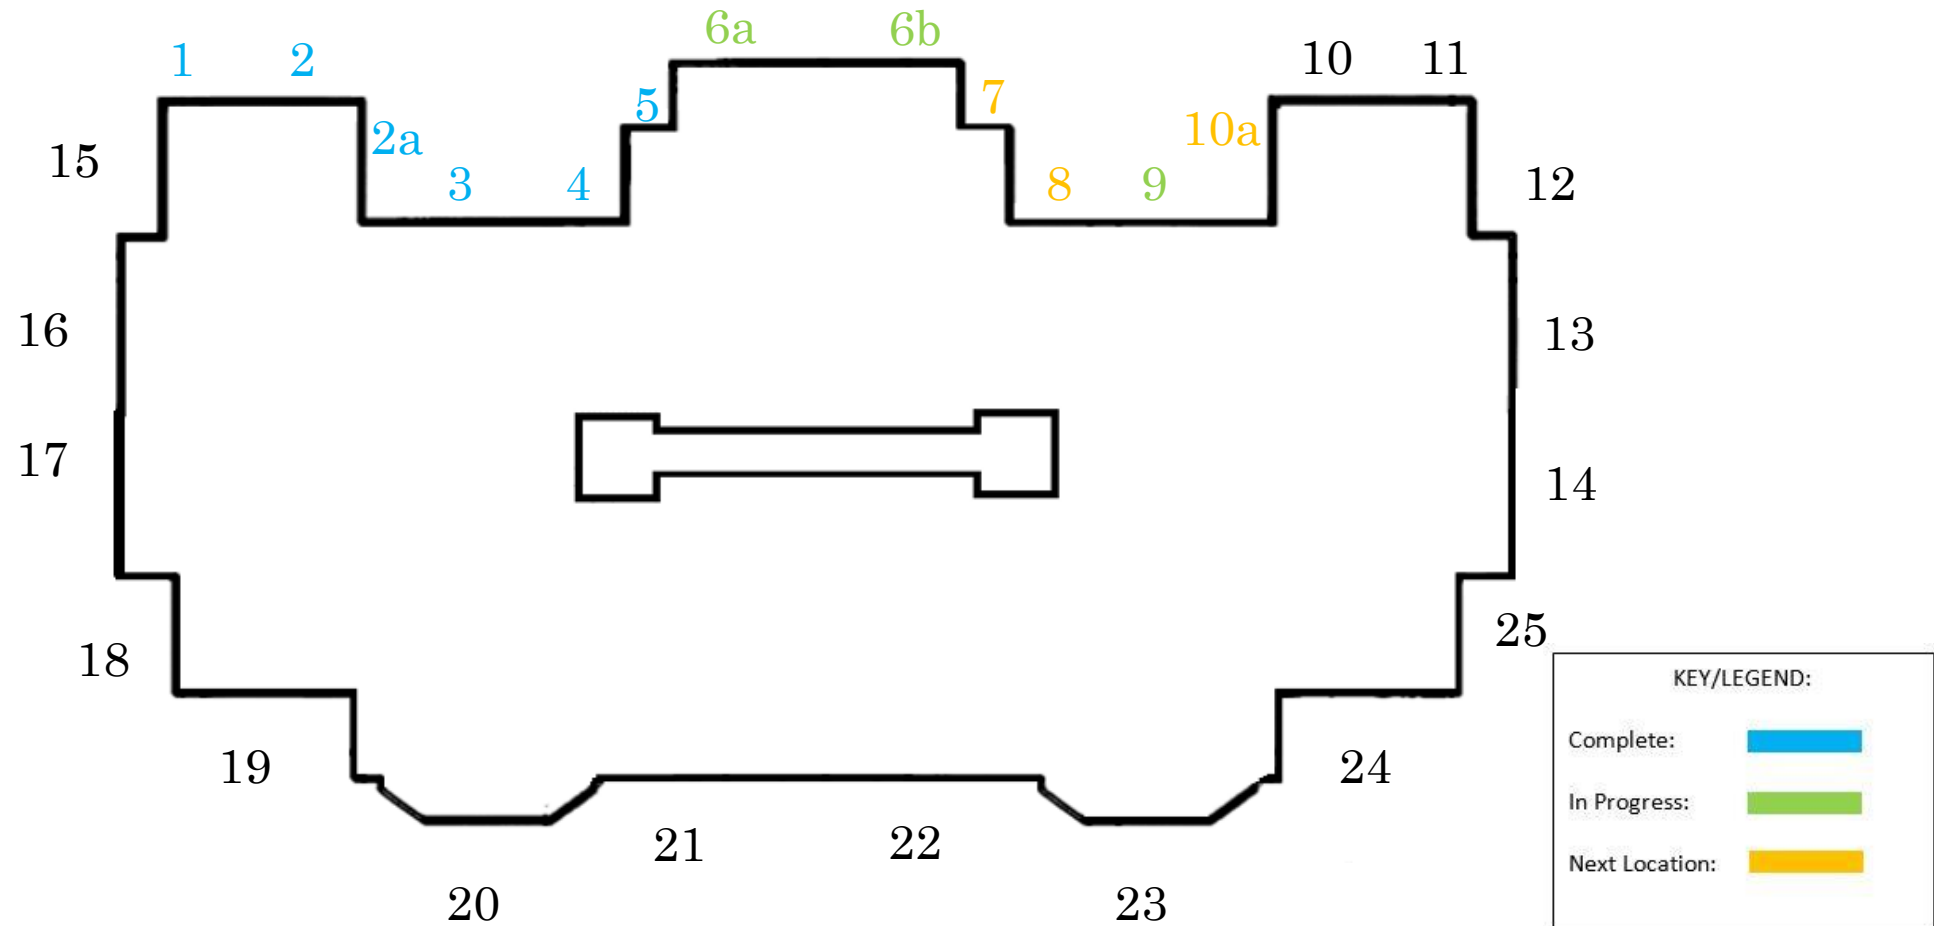

Swing Stage Drops – Leak Repairs – Tower 2

