



# Grand Panama Towers 1 & 2

Progress Report

3-17-23

# Schedule

- Lost Work Days:
  - 9/28/22 – Strong Winds
  - 9/29/22 – Strong Winds
  - 10/13/22 – Rain
  - 10/17/22 – Rain
  - 11/10/22 – Wind/Rain
  - 11/11/22 – Wind
  - 11/15/22 – Wind/Rain
  - 11/25/22 – Fog/Humidity
  - 11/30/22 – Rain
  - 12/8/22 – Heavy Fog/Humidity
  - 12/14/22 – Strong Wind/Rain
  - 12/20/22 – Rain
  - 12/23/22 – Freezing Temperatures
  - 1/3/23 – Rain
  - 1/4/23 – Rain
  - 1/27/23 – Rain
  - 1/30/23 – Heavy Fog/Humidity
  - 1/31/23 – Rain
  - 2/1/23 – Heavy Fog/Humidity
  - 2/2/23 – Rain/Humidity
  - 2/3/23 – Rain/Humidity
  - 3/3/23 – Wind
  - 3/7/23 – Wind
  - 3/13/23 – Rain/Humidity

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	2022							Qtr 4, 2022			Qtr 1, 2023			Qtr 2, 2023			Qtr 3				
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul									
1		<b>Project Duration</b>	<b>207 days</b>	<b>Tue 9/6/22</b>	<b>Wed 6/21/23</b>																						
2		<b>Mobilize</b>	6 days	Tue 9/6/22	Tue 9/13/22																						
3		<b>Tower 1</b>	<b>114 days</b>	<b>Wed 9/14/22</b>	<b>Mon 2/20/23</b>																						
4		North Elevation	25 days	Wed 9/14/22	Tue 10/18/22	2																					
5		East Elevation	7 days	Wed 10/19/22	Thu 10/27/22	4																					
6		West Elevation	7 days	Fri 10/28/22	Mon 11/7/22	5																					
7		South Elevation	75 days	Tue 11/8/22	Mon 2/20/23	6																					
8		<b>Tower 2</b>	<b>183 days</b>	<b>Mon 10/3/22</b>	<b>Wed 6/14/23</b>																						
9		North Elevation	7 days	Tue 4/25/23	Wed 5/3/23	12																					
10		West Elevation	30 days	Thu 5/4/23	Wed 6/14/23	9																					
11		South Elevation	20 days	Mon 10/3/22	Fri 10/28/22																						
12		East Elevation	45 days	Tue 2/21/23	Mon 4/24/23	7																					
13		<b>Tower 2 Garage</b>	30 days	Tue 3/14/23	Mon 4/24/23	14																					
14		<b>Separate Garage</b>	15 days	Tue 2/21/23	Mon 3/13/23	7																					
15		<b>Tower 2 - Misc. Leak Repairs</b>	20 days	Mon 10/3/22	Fri 10/28/22																						
16		<b>Demobilize</b>	5 days	Thu 6/15/23	Wed 6/21/23	10																					


  

Project: Grand Panama - Prelim Date: Thu 3/16/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
Inactive Milestone		Finish-only				

# Areas in Progress



# Swing Stage Drops – Tower 2

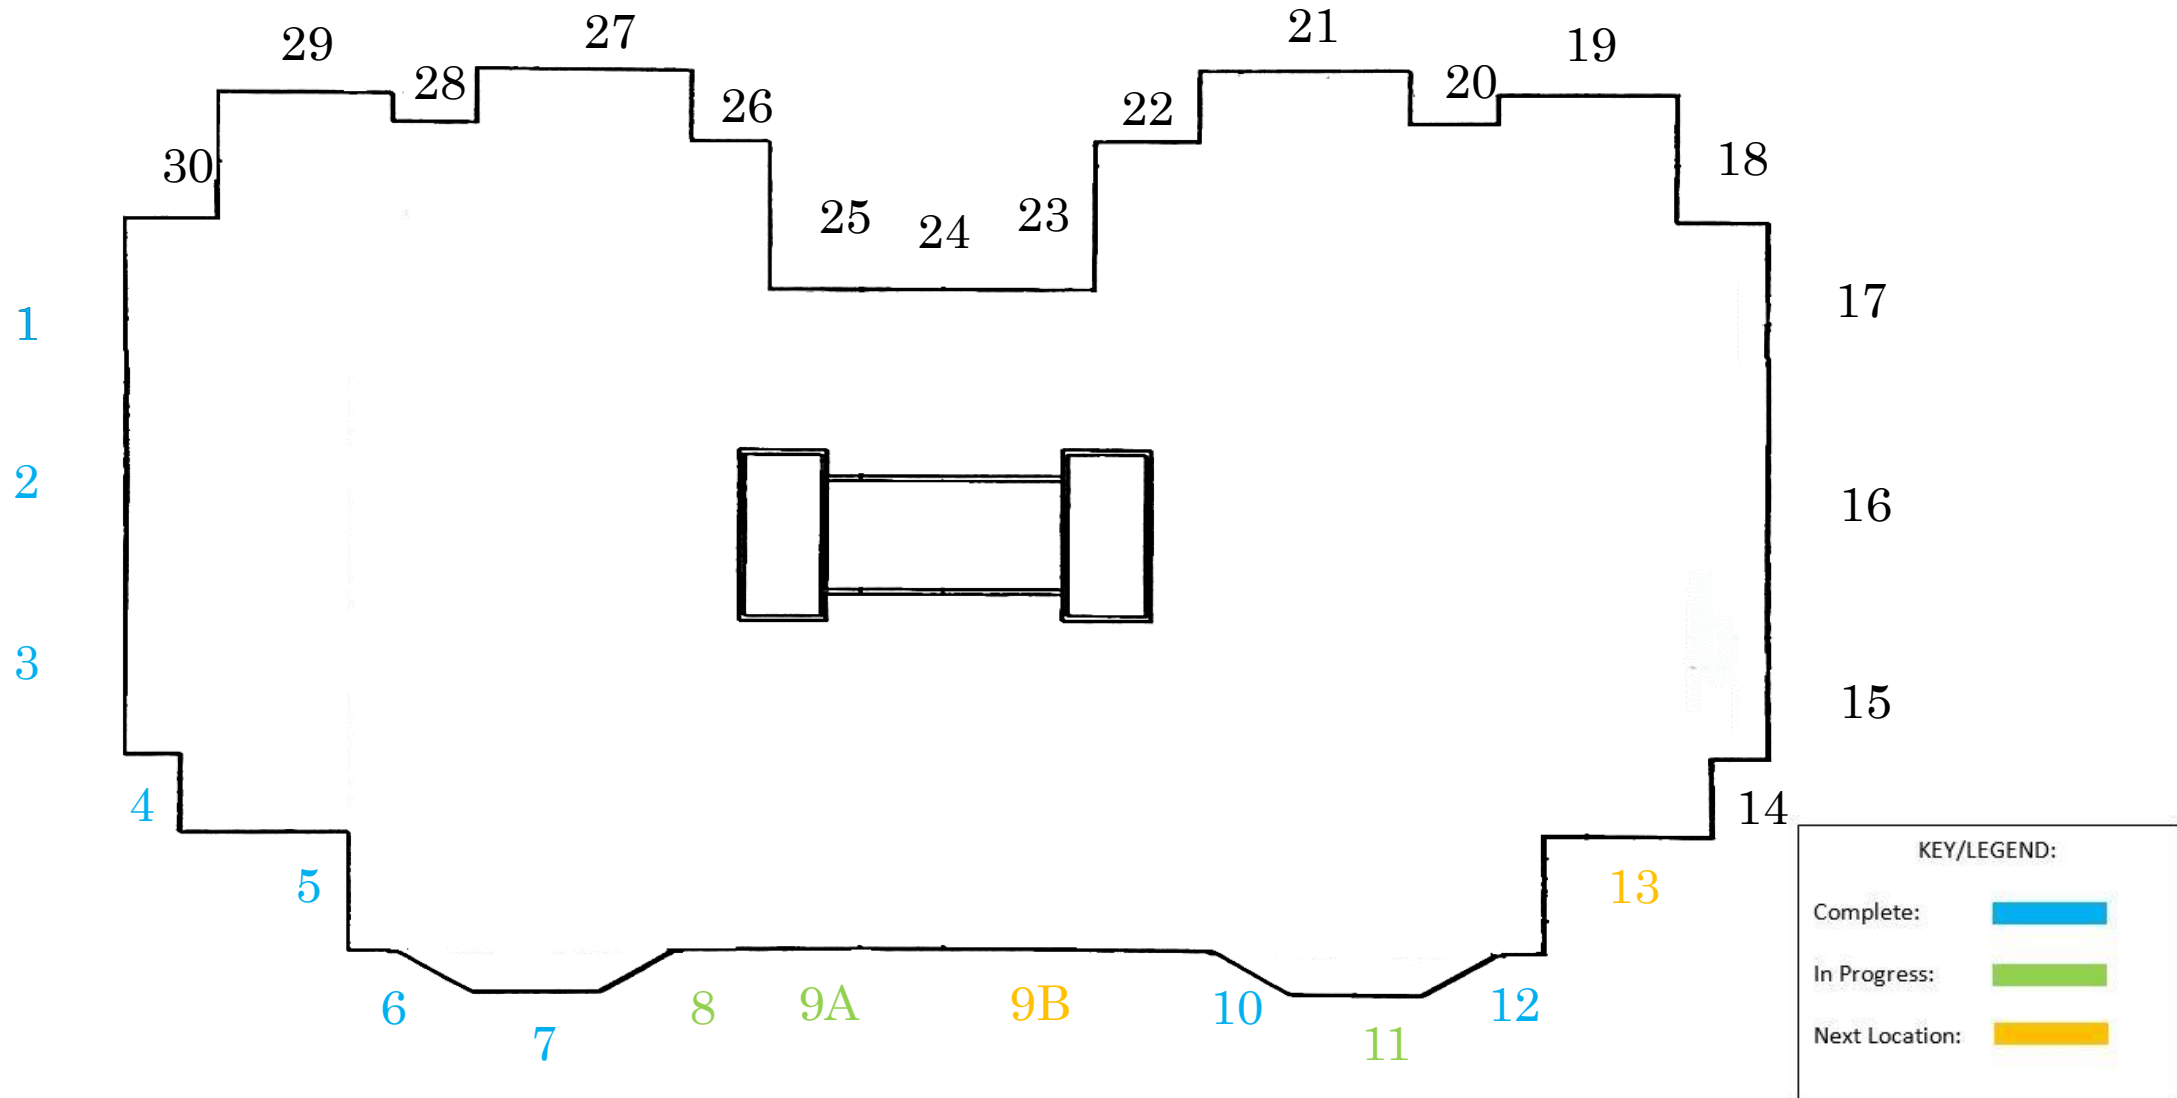

# Swing Stage Drops – Tower 1

