



Grand Panama Towers 1 & 2

Progress Report

3-24-23

Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	2022											
							Aug	Sep	Qtr 4, 2022		Qtr 1, 2023			Qtr 2, 2023			Qtr 3	
							Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul		
1		Project Duration	207 days	Tue 9/6/22	Wed 6/21/23													
2		Mobilize	6 days	Tue 9/6/22	Tue 9/13/22													
3		Tower 1	114 days	Wed 9/14/22	Mon 2/20/23													
4		North Elevation	25 days	Wed 9/14/22	Tue 10/18/22													
5		East Elevation	7 days	Wed 10/19/22	Thu 10/27/22													
6		West Elevation	7 days	Fri 10/28/22	Mon 11/7/22													
7		South Elevation	75 days	Tue 11/8/22	Mon 2/20/23													
8		Tower 2	183 days	Mon 10/3/22	Wed 6/14/23													
9		North Elevation	7 days	Tue 4/25/23	Wed 5/3/23	12												
10		West Elevation	30 days	Thu 5/4/23	Wed 6/14/23	9												
11		South Elevation	20 days	Mon 10/3/22	Fri 10/28/22													
12		East Elevation	45 days	Tue 2/21/23	Mon 4/24/23	7												
13		Tower 2 Garage	30 days	Mon 4/3/23	Fri 5/12/23													
14		Separate Garage	15 days	Tue 2/21/23	Mon 3/13/23	7												
15		Tower 2 - Misc. Leak Repairs	20 days	Mon 10/3/22	Fri 10/28/22													
16		Demobilize	5 days	Thu 6/15/23	Wed 6/21/23	10												

- Lost Work Days:
 - 9/28/22 – Strong Winds
 - 9/29/22 – Strong Winds
 - 10/13/22 – Rain
 - 10/17/22 – Rain
 - 11/10/22 – Wind/Rain
 - 11/11/22 – Wind
 - 11/15/22 – Wind/Rain
 - 11/25/22 – Fog/Humidity
 - 11/30/22 – Rain
 - 12/8/22 – Heavy Fog/Humidity
 - 12/14/22 – Strong Wind/Rain
 - 12/20/22 – Rain
 - 12/23/22 – Freezing Temperatures
 - 1/3/23 – Rain
 - 1/4/23 – Rain
 - 1/27/23 – Rain
 - 1/30/23 – Heavy Fog/Humidity
 - 1/31/23 – Rain
 - 2/1/23 – Heavy Fog/Humidity
 - 2/2/23 – Rain/Humidity
 - 2/3/23 – Rain/Humidity
 - 3/3/23 – Wind
 - 3/7/23 – Wind
 - 3/13/23 – Rain/Humidity


Project: Grand Panama - Prelim
Date: Fri 3/24/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Areas in Progress



Swing Stage Drops – Tower 2

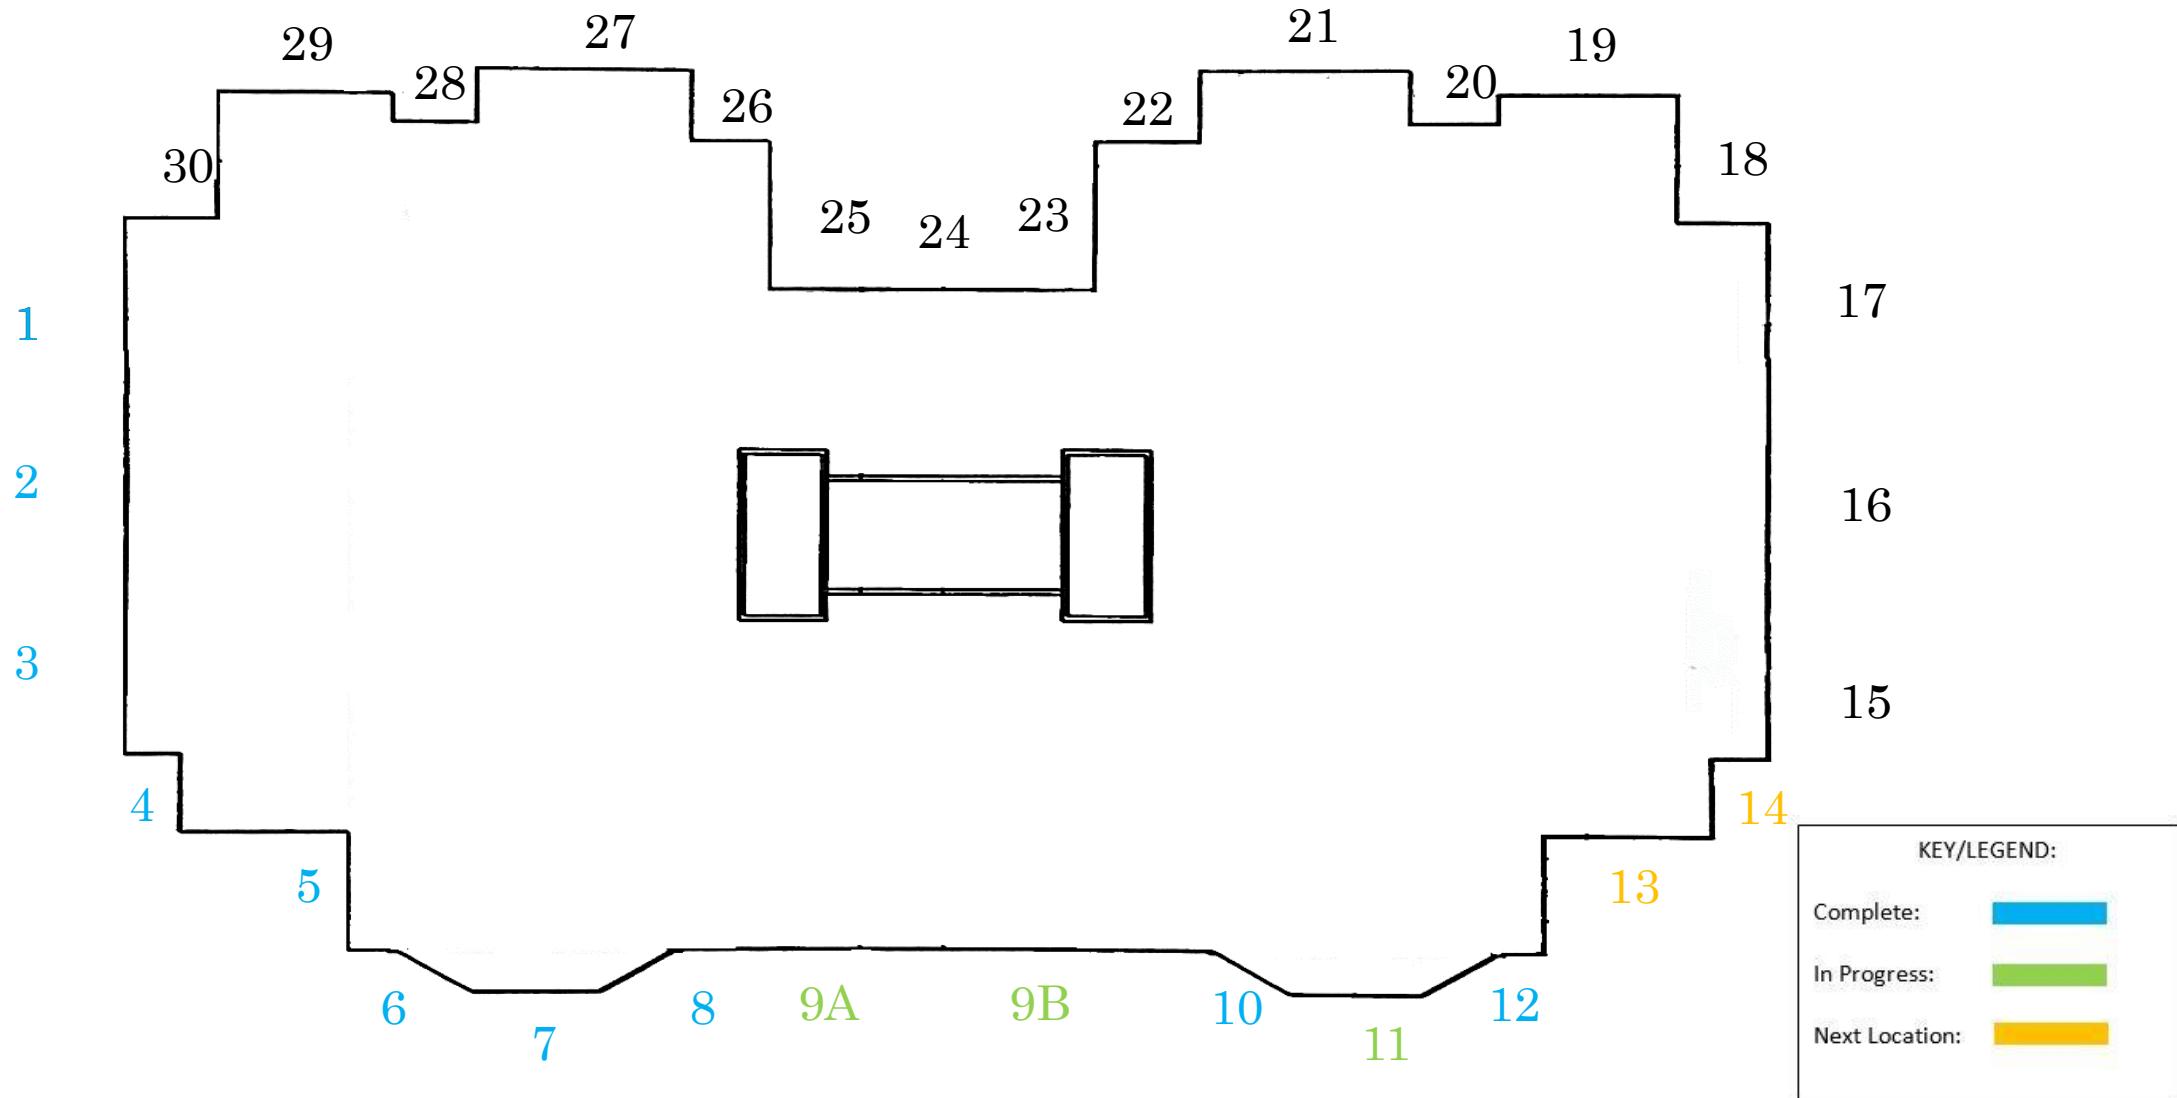

Swing Stage Drops – Tower 1

