

Grand Panama Towers 1 & 2

Progress Report

4-21-23



Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	Q22		Qtr 4, 2022				Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023
						Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	
1		Project Duration	202 days	Tue 9/6/22	Wed 6/14/23													
2		Mobilize	6 days	Tue 9/6/22	Tue 9/13/22													
3		Tower 1	114 days	Wed 9/14/22	Mon 2/20/23													
4		North Elevation	25 days	Wed 9/14/22	Tue 10/18/22													
5		East Elevation	7 days	Wed 10/19/22	Thu 10/27/22													
6		West Elevation	7 days	Fri 10/28/22	Mon 11/7/22													
7		South Elevation	75 days	Tue 11/8/22	Mon 2/20/23													
8		Tower 2	178 days	Mon 10/3/22	Wed 6/7/23													
9		North Elevation	7 days	Tue 4/18/23	Wed 4/26/23													
10		West Elevation	30 days	Thu 4/27/23	Wed 6/7/23													
11		South Elevation	20 days	Mon 10/3/22	Fri 10/28/22													
12		East Elevation	40 days	Tue 2/21/23	Mon 4/17/23													
13		Tower 2 Garage	30 days	Mon 4/24/23	Fri 6/2/23													
14		Separate Garage	15 days	Tue 2/21/23	Mon 3/13/23													
15		Tower 2 - Misc. Leak Repairs	20 days	Mon 10/3/22	Fri 10/28/22													
16		Demobilize	5 days	Thu 6/8/23	Wed 6/14/23													


- Lost Work Days:
 - 9/28/22 – Strong Winds
 - 9/29/22 – Strong Winds
 - 10/13/22 – Rain
 - 10/17/22 – Rain
 - 11/10/22 – Wind/Rain
 - 11/11/22 – Wind
 - 11/15/22 – Wind/Rain
 - 11/25/22 – Fog/Humidity
 - 11/30/22 – Rain
 - 12/8/22 – Heavy Fog/Humidity
 - 12/14/22 – Strong Wind/Rain
 - 12/20/22 – Rain
 - 12/23/22 – Freezing Temperatures
 - 1/3/23 – Rain
 - 1/4/23 – Rain
 - 1/27/23 – Rain
 - 1/30/23 – Heavy Fog/Humidity
 - 1/31/23 – Rain
 - 2/1/23 – Heavy Fog/Humidity
 - 2/2/23 – Rain/Humidity
 - 2/3/23 – Rain/Humidity
 - 3/3/23 – Wind
 - 3/7/23 – Wind
 - 3/13/23 – Rain/Humidity
 - 4/3/23 – Rain
 - 4/13/23 – Rain/Wind
 - 4/14/23 – Rain

Project: Grand Panama - Prelim Date: Fri 4/21/23	Task		Inactive Summary		External Tasks
	Split		Manual Task		External Milestone
	Milestone		Duration-only		Deadline
	Summary		Manual Summary Rollup		Progress
	Project Summary		Manual Summary		Manual Progress
	Inactive Task		Start-only		
Inactive Milestone		Finish-only			

Areas in Progress

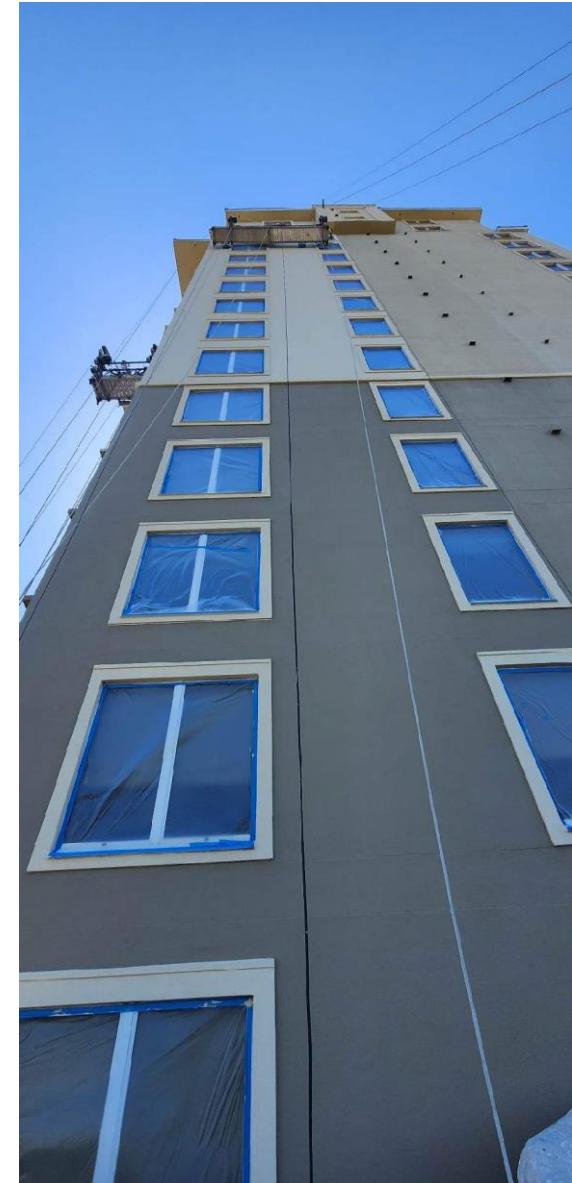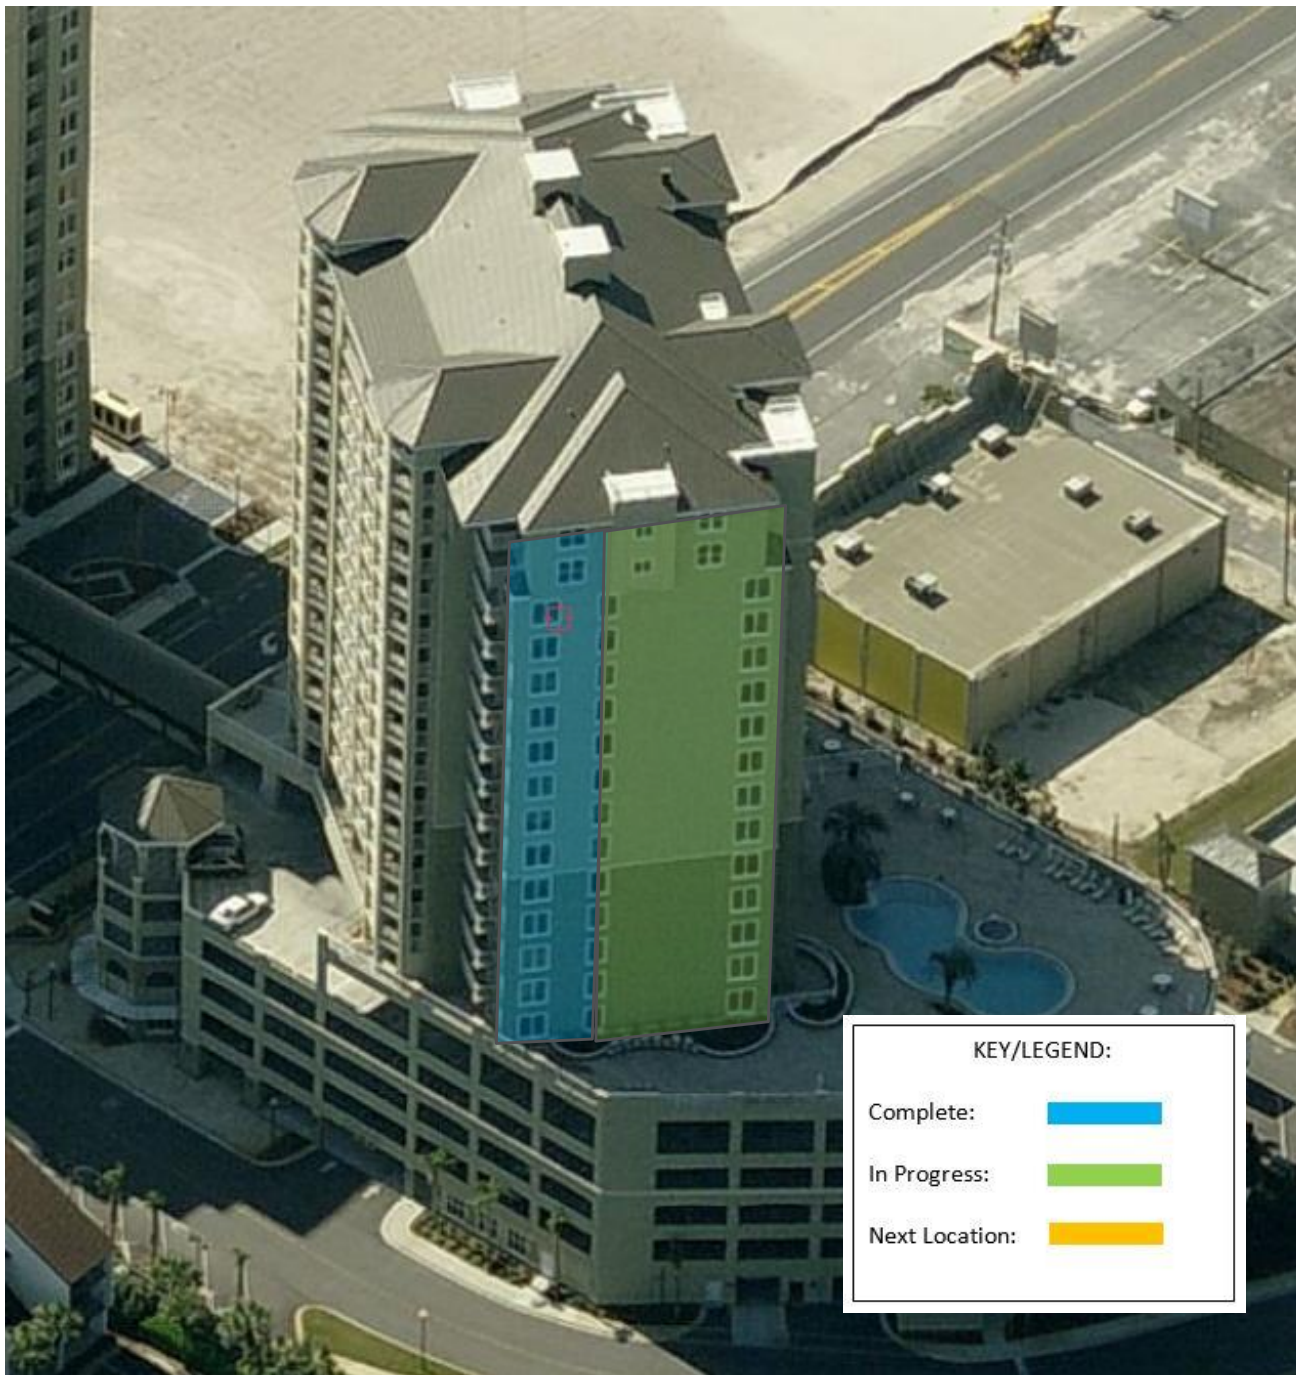

Swing Stage Drops – Tower 2

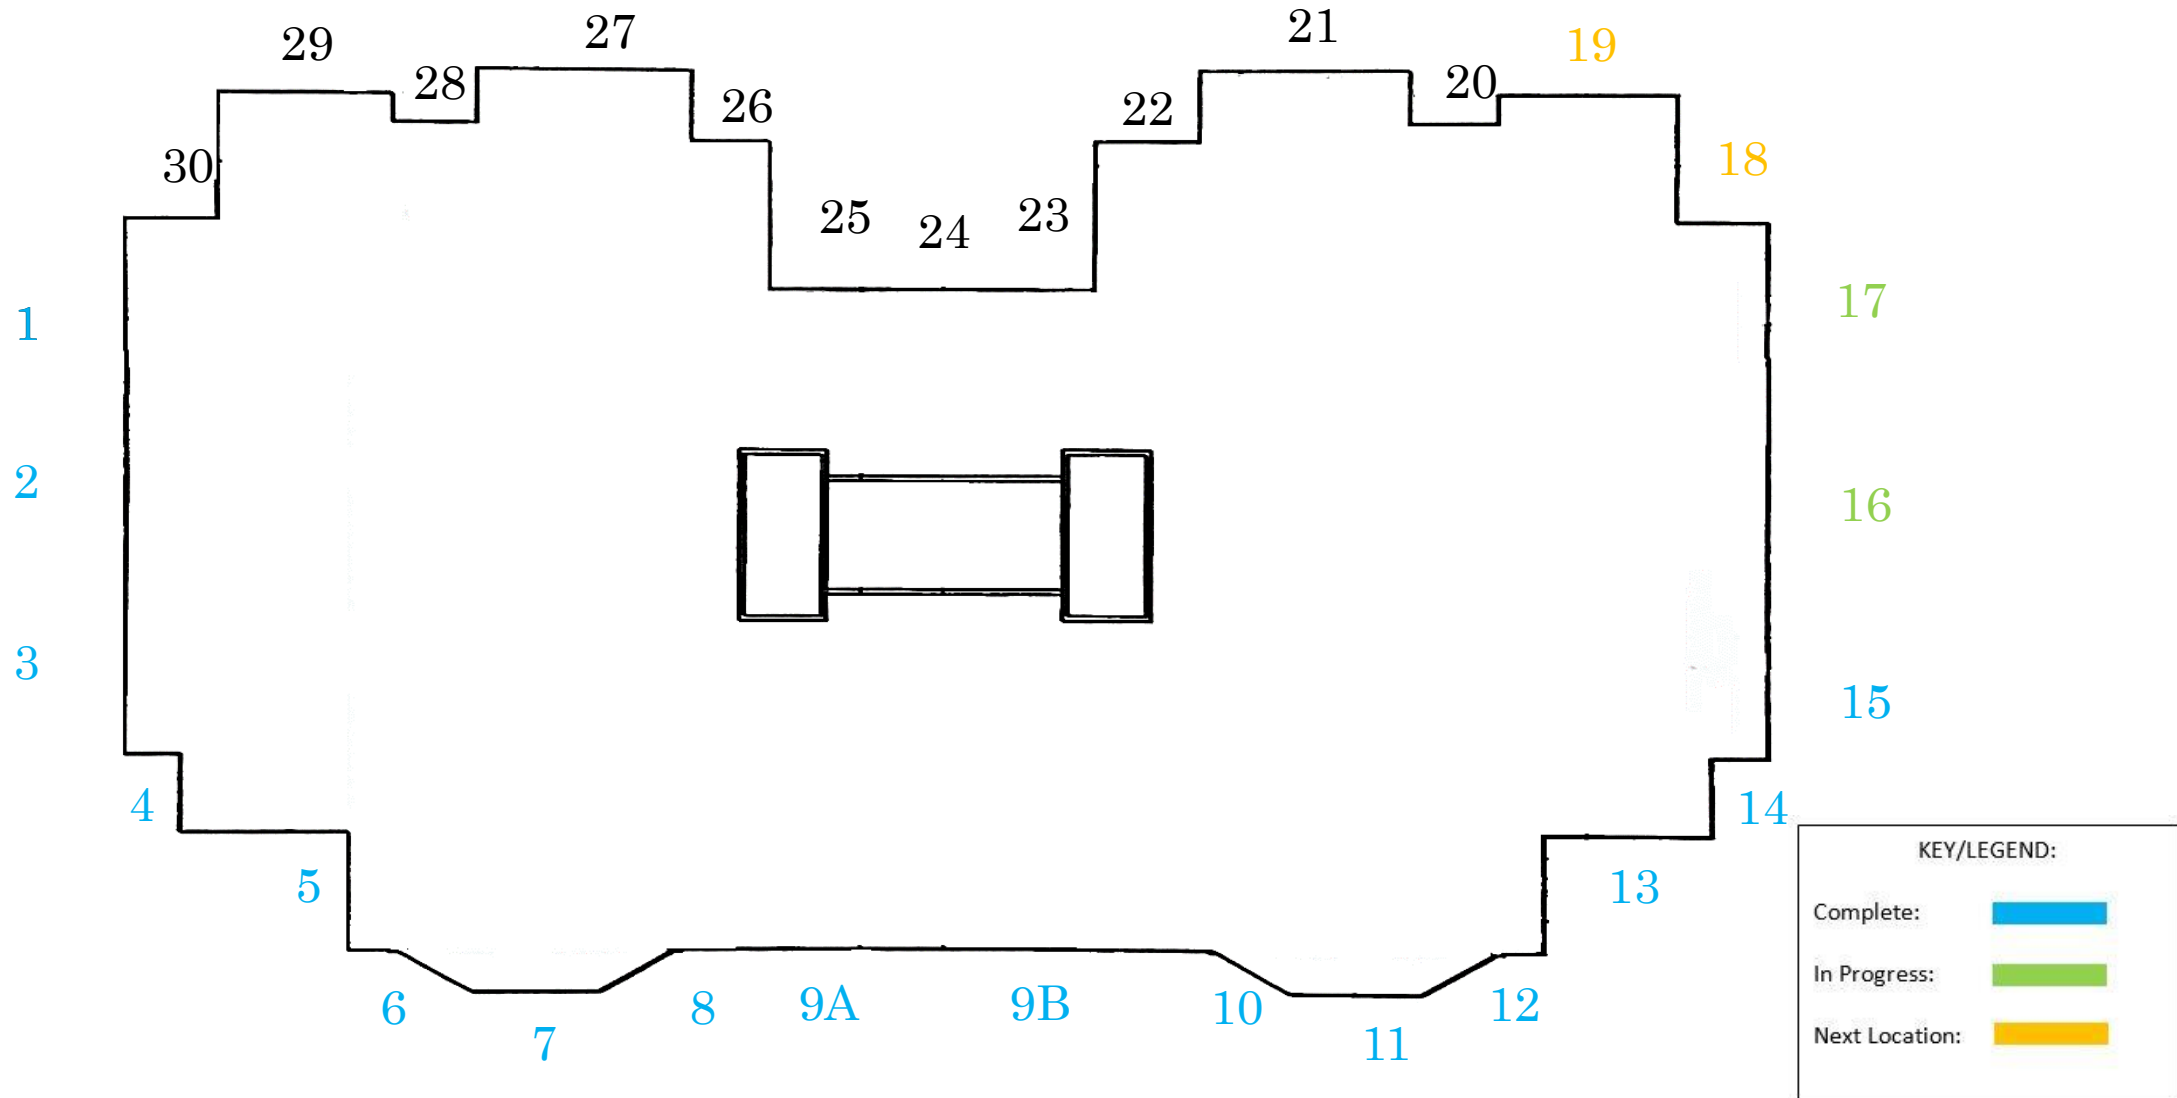

Swing Stage Drops – Tower 1

