


Grand Panama Towers 1 & 2

Progress Report

8-14-2023

Schedule

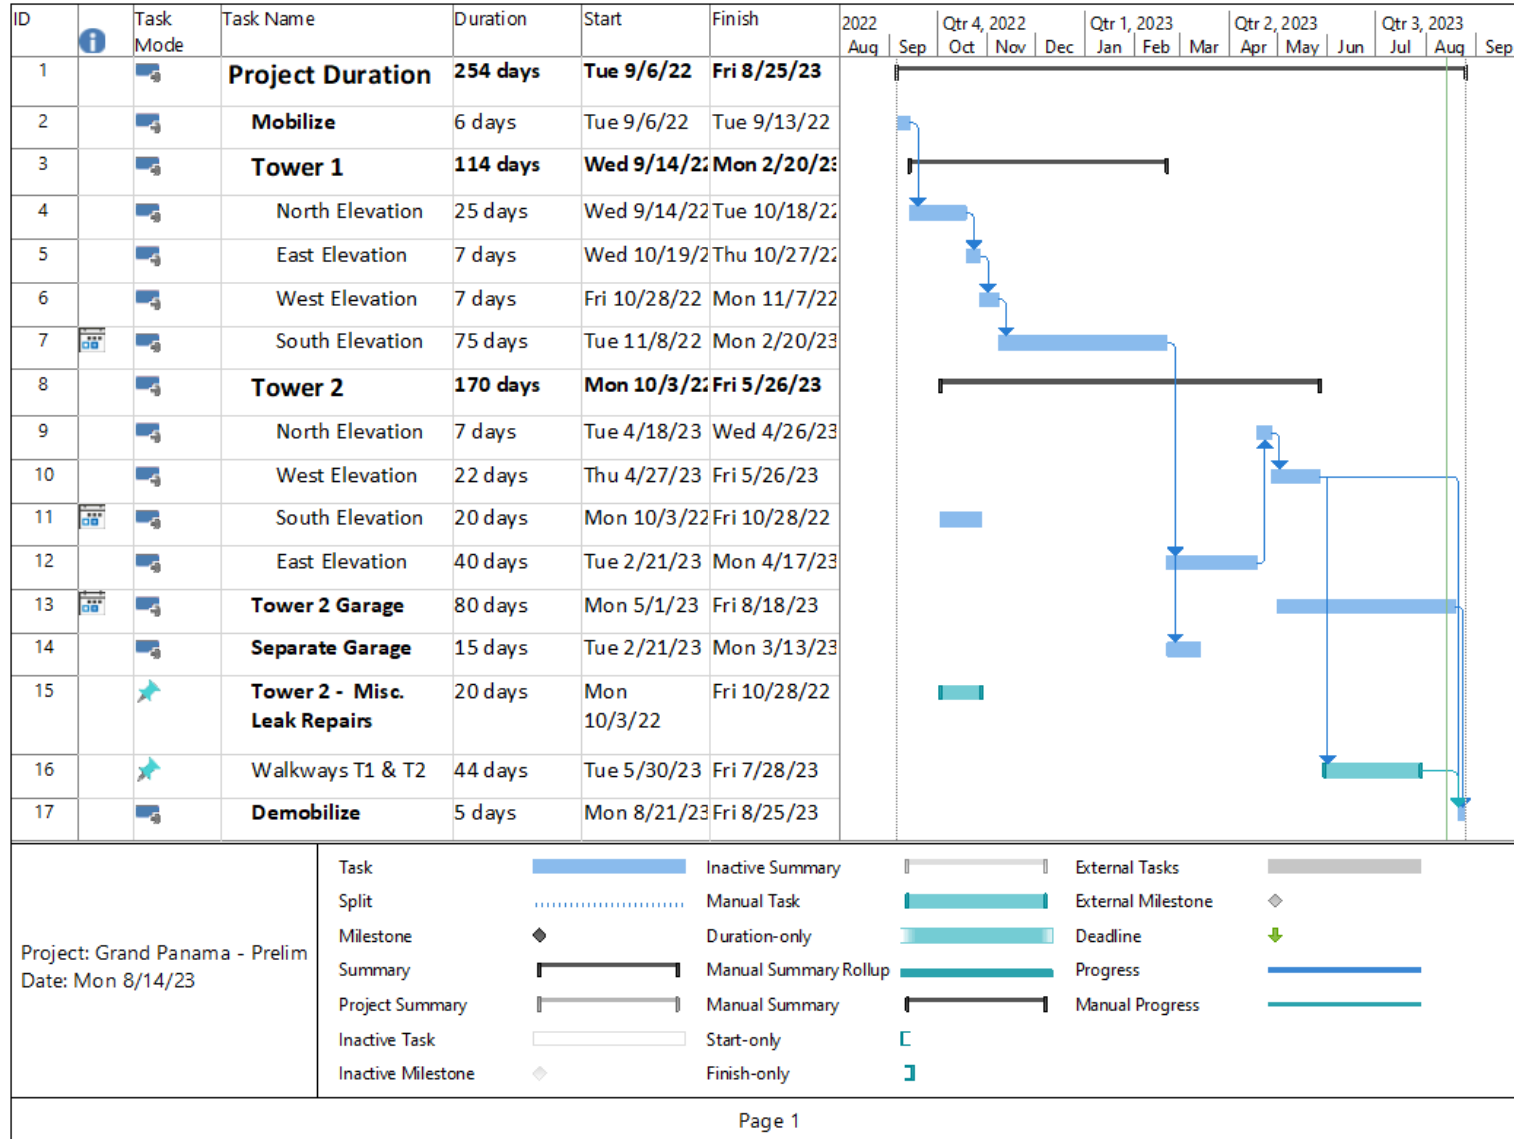

- Added the Walkway Coatings CO into the schedule

- Lost Work Days:

- 9/28/22 – Strong Winds
- 9/29/22 – Strong Winds
- 10/13/22 – Rain
- 10/17/22 – Rain
- 11/10/22 – Wind/Rain
- 11/11/22 – Wind
- 11/15/22 – Wind/Rain
- 11/25/22 – Fog/Humidity
- 11/30/22 – Rain
- 12/8/22 – Heavy Fog/Humidity
- 12/14/22 – Strong Wind/Rain
- 12/20/22 – Rain
- 12/23/22 – Freezing Temperatures
- 1/3/23 – Rain
- 1/4/23 – Rain
- 1/27/23 – Rain
- 1/30/23 – Heavy Fog/Humidity
- 1/31/23 – Rain
- 2/1/23 – Heavy Fog/Humidity
- 2/2/23 – Rain/Humidity
- 2/3/23 – Rain/Humidity
- 3/3/23 – Wind
- 3/7/23 – Wind
- 3/13/23 – Rain/Humidity
- 4/3/23 – Rain
- 4/13/23 – Rain/Wind
- 4/14/23 – Rain
- 4/27/23 – Rain/Wind
- 6/15/23 – Humidity/Rain
- 6/19/23 – Rain
- 7/10/23 – Rain
- 7/13/23 – Rain



Areas in Progress


The garage and pergola coating is wrapping up. We will begin coating the drive through in the bottom of the garage.



Painted Pergolas

KEY/LEGEND:	
Complete:	
In Progress:	
Next Location:	

Swing Stage Drops – Tower 2

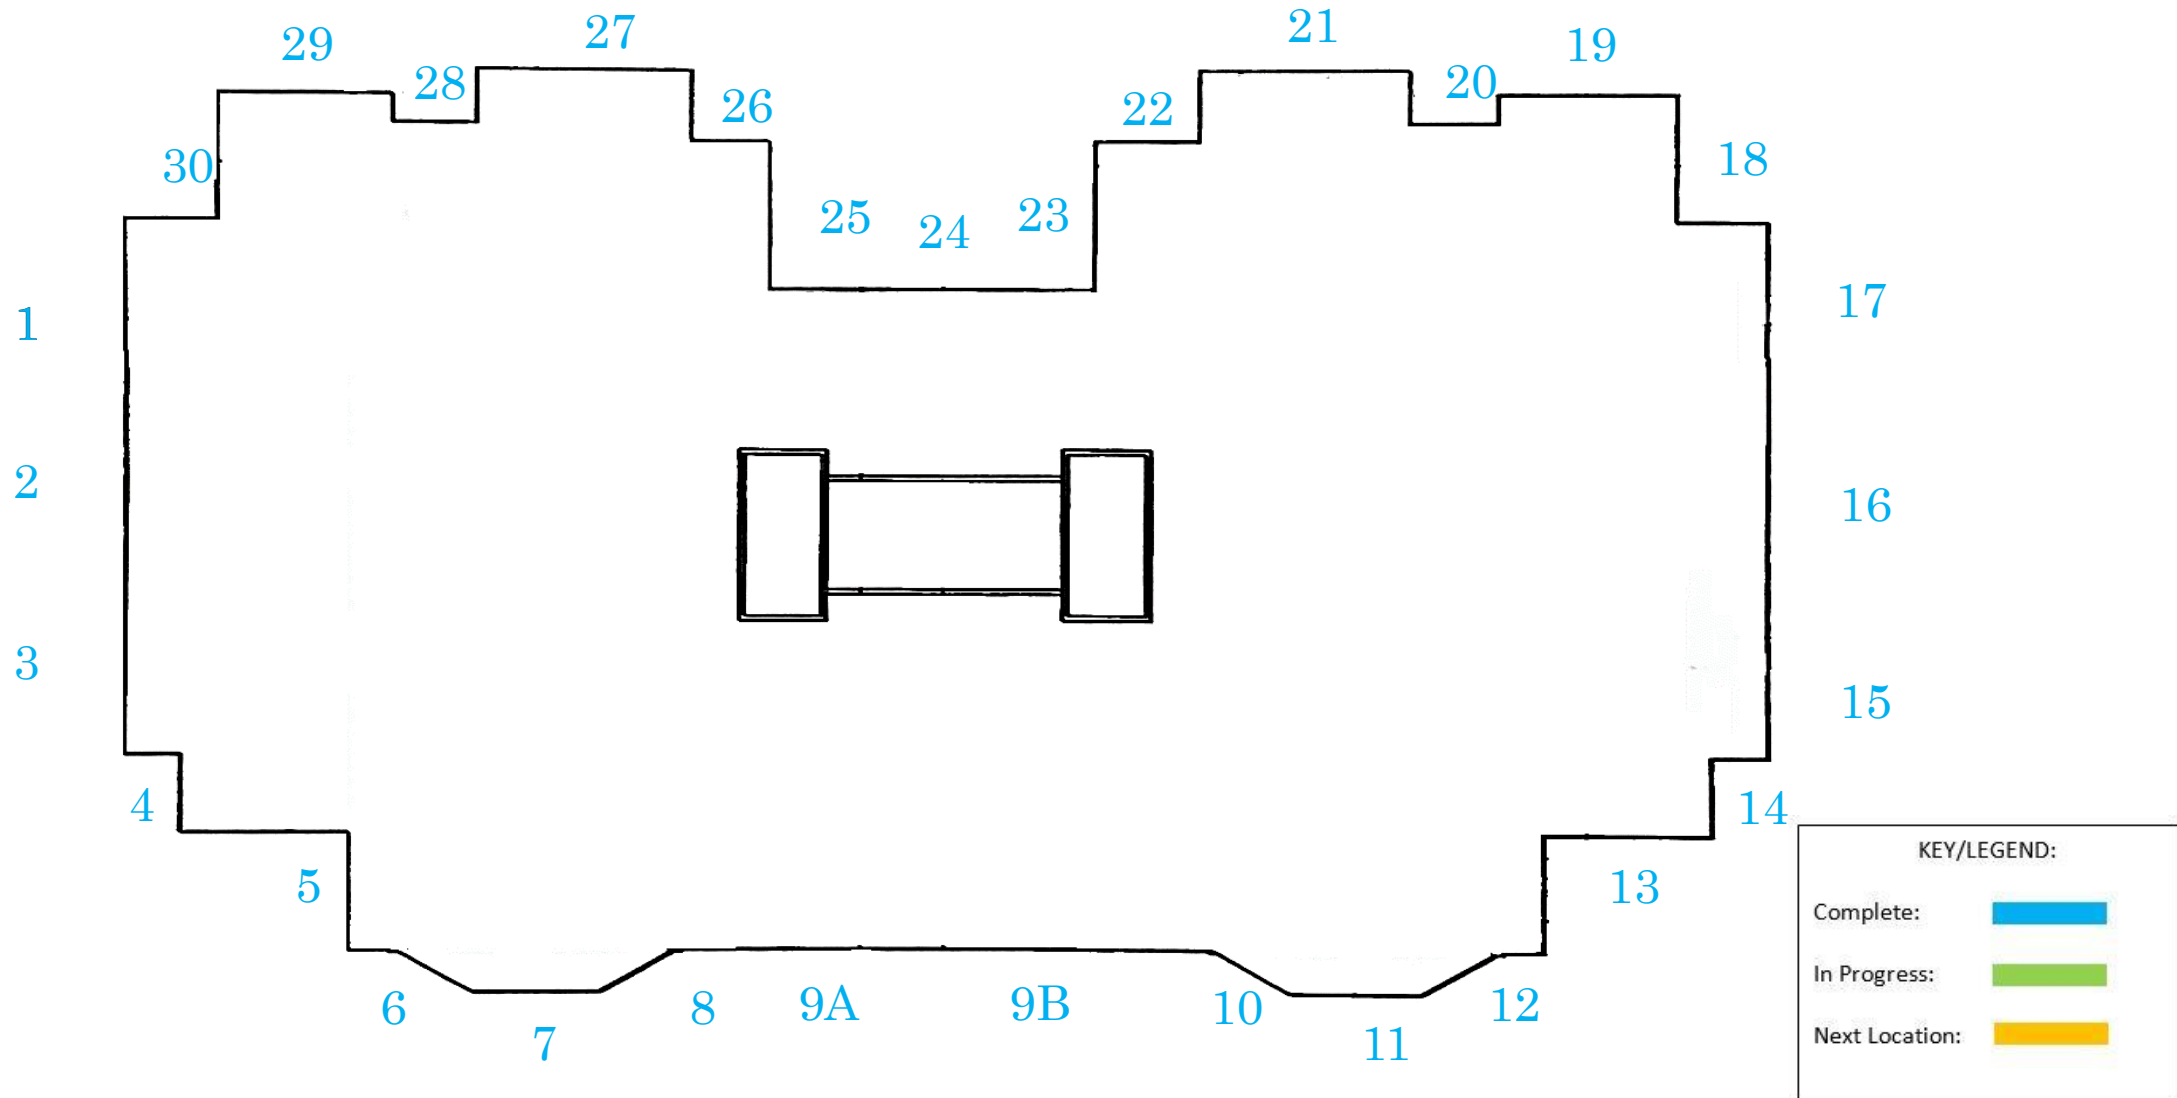

Swing Stage Drops – Tower 1

