




# Grand Panama Beach Resort

## N Tower Garage Repairs Progress Report



---

April 8<sup>th</sup>, 2024

*Scope of Work: Surface prep  
and repairs, coatings*

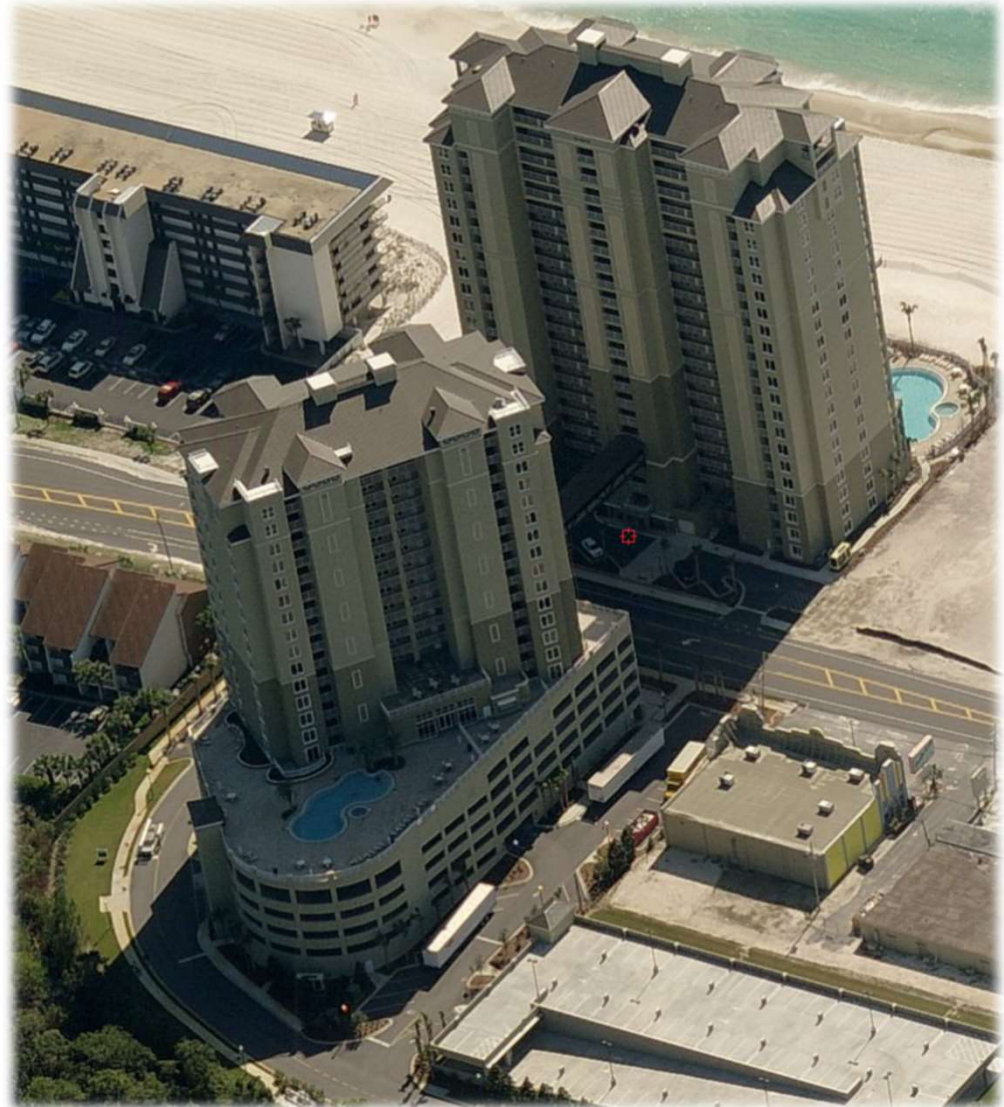



## Project Progress

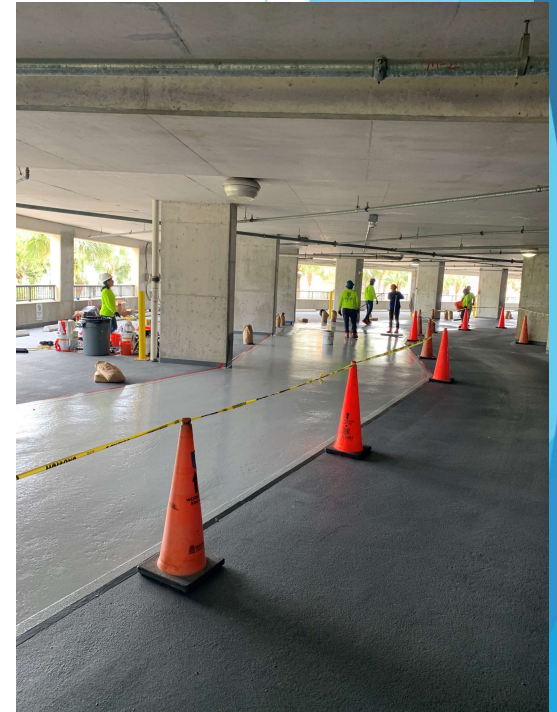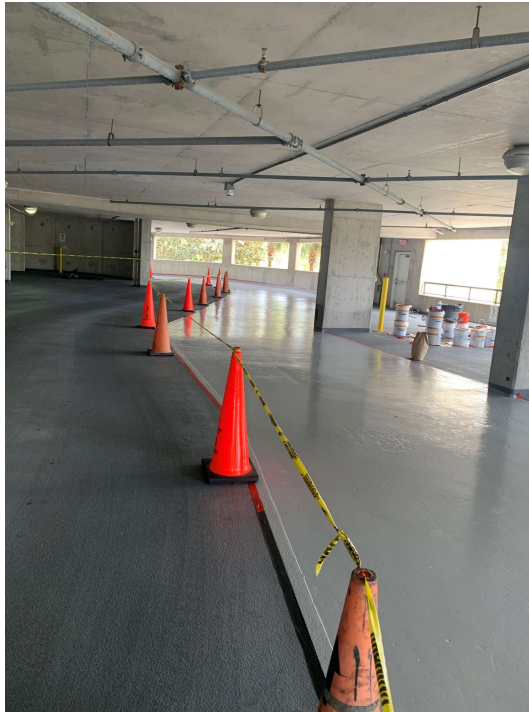

- ▶ Traffic Coating on Level 2 - final travel lane.



## Project Progress

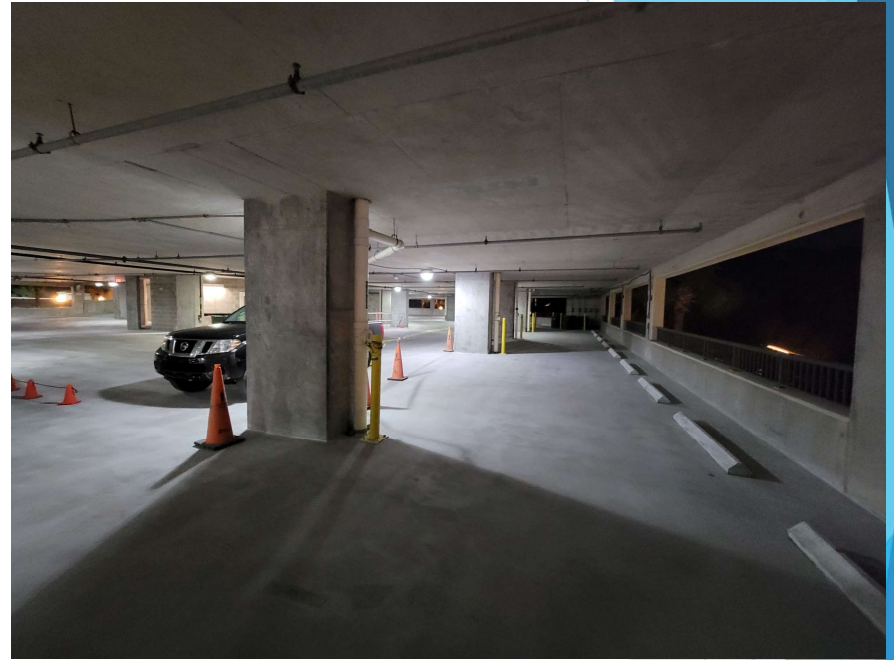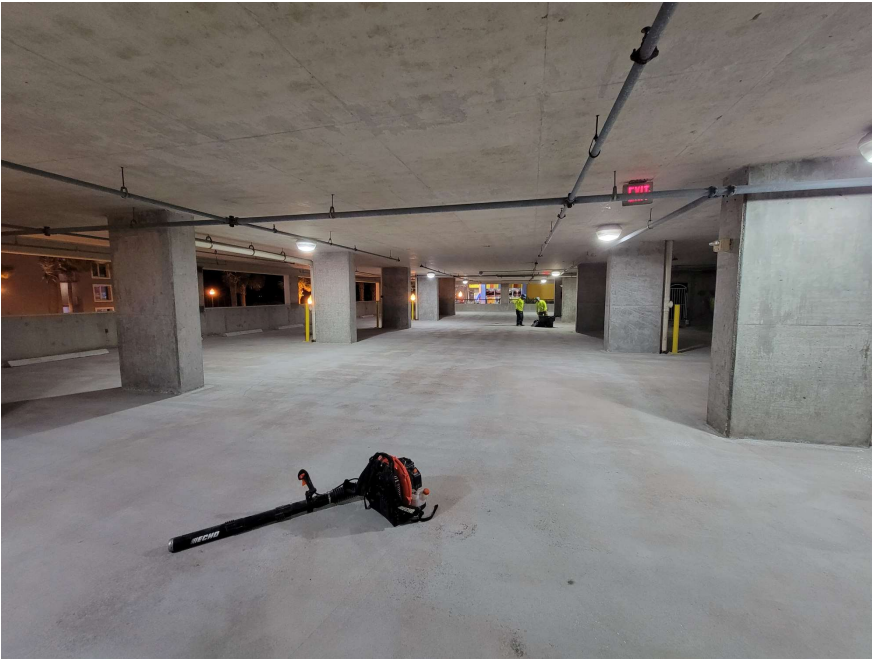

- ▶ Level 2 - Phase 2 (Outside half) , shotblast completed ready for traffic coating.

# Grand Panama Beach Resort Schedule Look Ahead

## ► Week 1: 4/8/24

Level 5 - Complete, open to traffic

Level 2 - Phases 2 and 3 complete, traffic redirected to allow continued access to upper levels

Exit Ramp - North travel lane complete, south lane first intermediate coat is in progress. Complete by the end of the week.

Striping to be completed over the weekend and all levels open to traffic the week of 4/15/24

